Neighbourhood Plan Project Timeline Apr 2022-May 2024

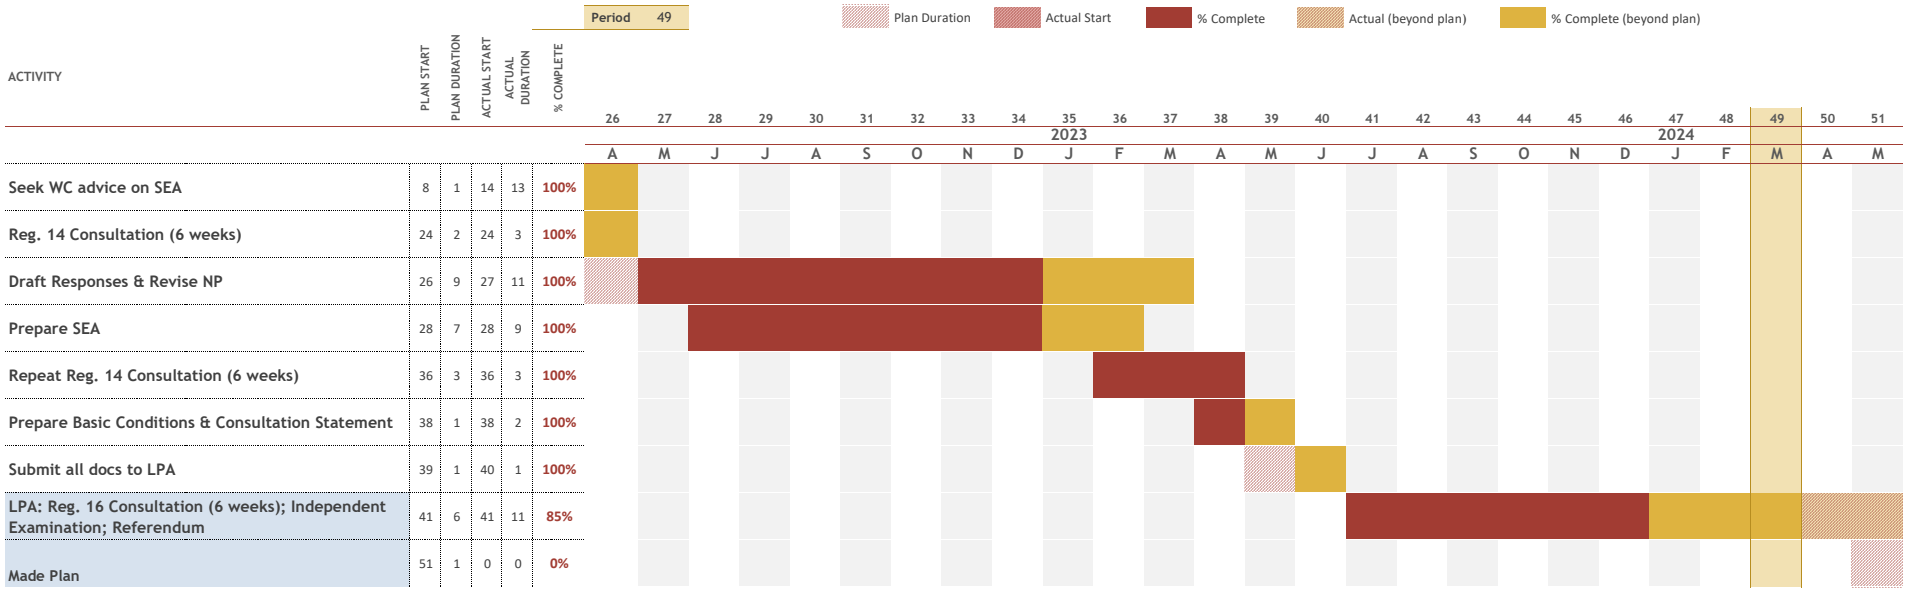

ACTIVITY	PLAN START	PLAN DURATION	ACTUAL START	ACTUAL DURATION	% COMPLETE
Seek WC advice on SEA	8	1	14	13	100%
Reg. 14 Consultation (6 weeks)	24	2	24	3	100%
Draft Responses & Revise NP	26	9	27	11	100%
Prepare SEA	28	7	28	9	100%
Repeat Reg. 14 Consultation (6 weeks)	36	3	36	3	100%
Prepare Basic Conditions & Consultation Statement	38	1	38	2	100%
Submit all docs to LPA	39	1	40	1	100%
LPA: Reg. 16 Consultation (6 weeks); Independent Examination; Referendum	41	6	41	11	85%
Made Plan	51	1	0	0	0%
